REQUEST FOR BIDDING INTERPRETATION (RFBI)

(Email no later than December 17, 2024, 5:00 p.m.)

To: Sagar Gupta, Project Director

Project Management and Development Branch

Real Estate Services Division

Phone: 916-591-2691

Email: sagar.gupta@dgs.ca.gov

PMDB RFBI No.: 6

Requestor RFBI No.: 3

Request Date: Dec. 17, 2024

From (Bidder): Preston Pipelines Infrastructure LLC

Contact: Chad Hutchinson

Phone: 209.649.5982 Fax: 916.386.7531

Email: chutchinson@prestonpipelines.com

All RFBIs received prior to deadline identified above, and responses from the State will be published on http://www.caleprocure.ca.gov. Click on "Start Search." In the event name field, enter the project number and click search. While viewing the Event Details, click on "View Event Package" to view RFBI responses.

Project No.: 000000000008666

Project Name: DSH-Coalinga Hydronic Loop Replacement

Location: Coalinga, CA

Drawing Reference: Civil Sheet C-4.3 Project Manual Reference: 23 20 00 - Valves

Question: Note 22 on the plan sheets states to install the ARV inside a gate valve vault per Detail

6/C-4.3. However, there is no Detail 6 on Plan Sheet C-4.3.

Can the plans be revised to include a detail showing the ARV installation within the valve

vauit?


<u>Response:</u> Install ARV assembly per the attached City of Fresno Standard W-13. Use only the portion of the detail W-13 indicated.

By: Bureau Veritas, Orland Obtera (949.210.5781), 1-10-2025

Plan Note

INSTALL 1" AIR RELEASE VALVES, MUELLER CO, MODEL NUMBER 330AR1884—BLN ON SUPPLY & RETURN LINES PER MANUFACTURER'S SPECS; INSTALL INSIDE GATE VALVE VAULT

PER DETAIL 6/C-4.3 WHERE POSSIBLE, INSTALL WITH SHELL ASSEMBLY OTHERWISE

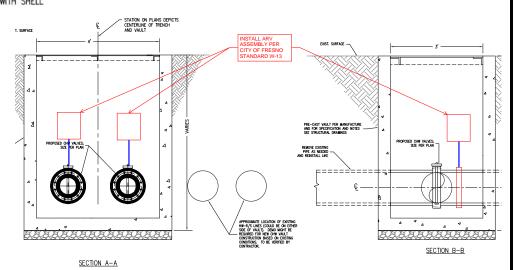

Bidder's Authorized Signature:

[] Check here if additional pages attached

Page 1 of

RESDMSTR: REV. 6.3.2021 Appendix 00 21 00.1 Project Number: 000000000008666

